




Gloria D 40 (270x270)

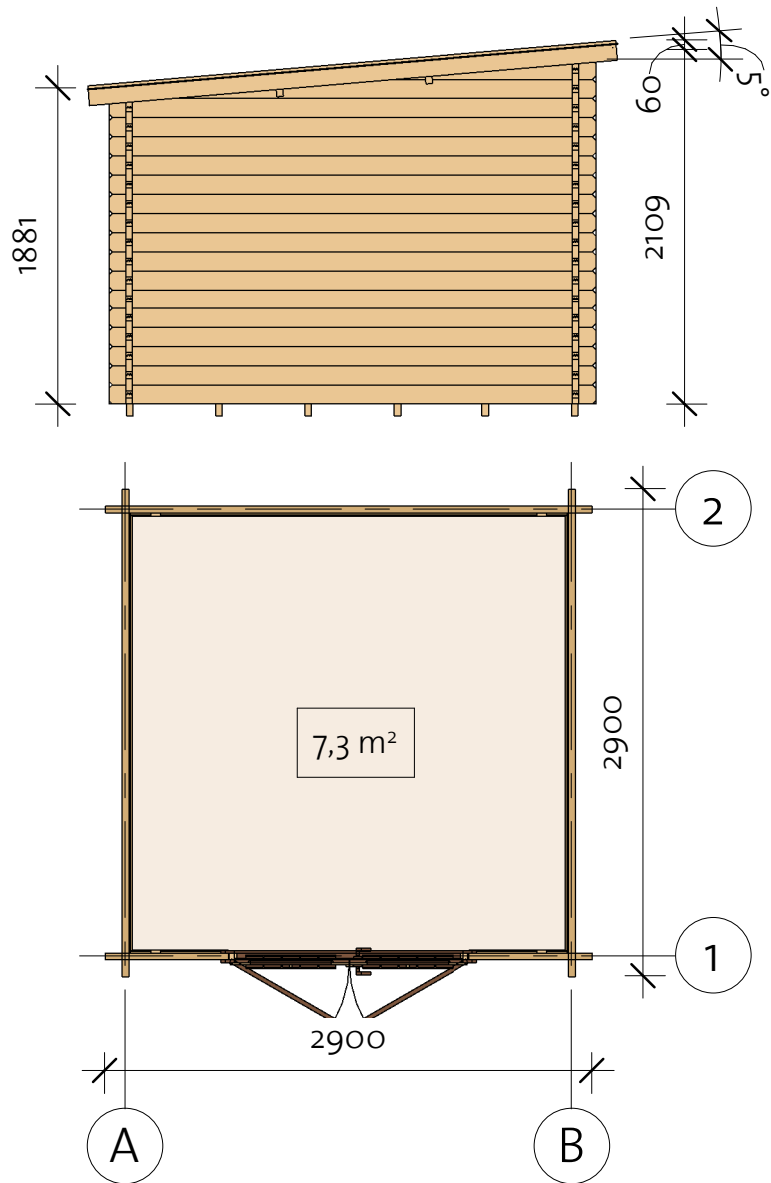

Gloria D 40 (270x270)

Foundation

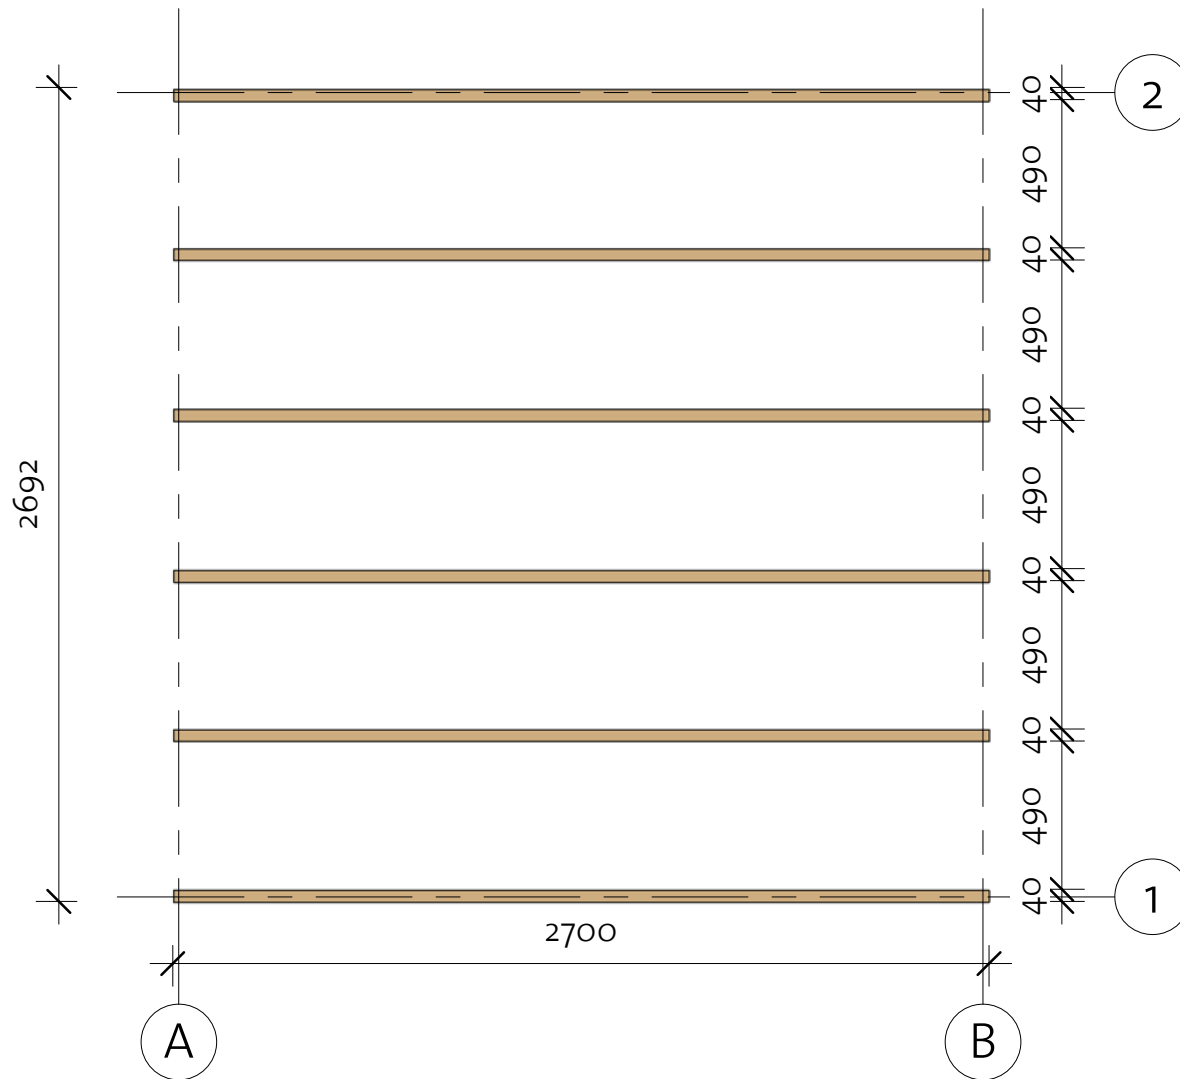




Impregnated foundation beams				
Mark	Type	Profile	Count	Length
IFB	IFB 40x70		6	2700

Gloria D 40 (270x270)


Floor Plan

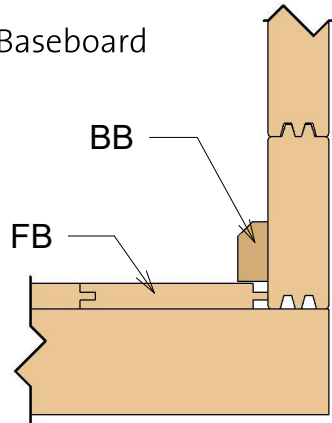① Baseboard




Floor Schedule				
Mark	Type	Profile	Count	Length
FB	FB 17x114		24	2617
BB	BB 20x40		4	2700

190827

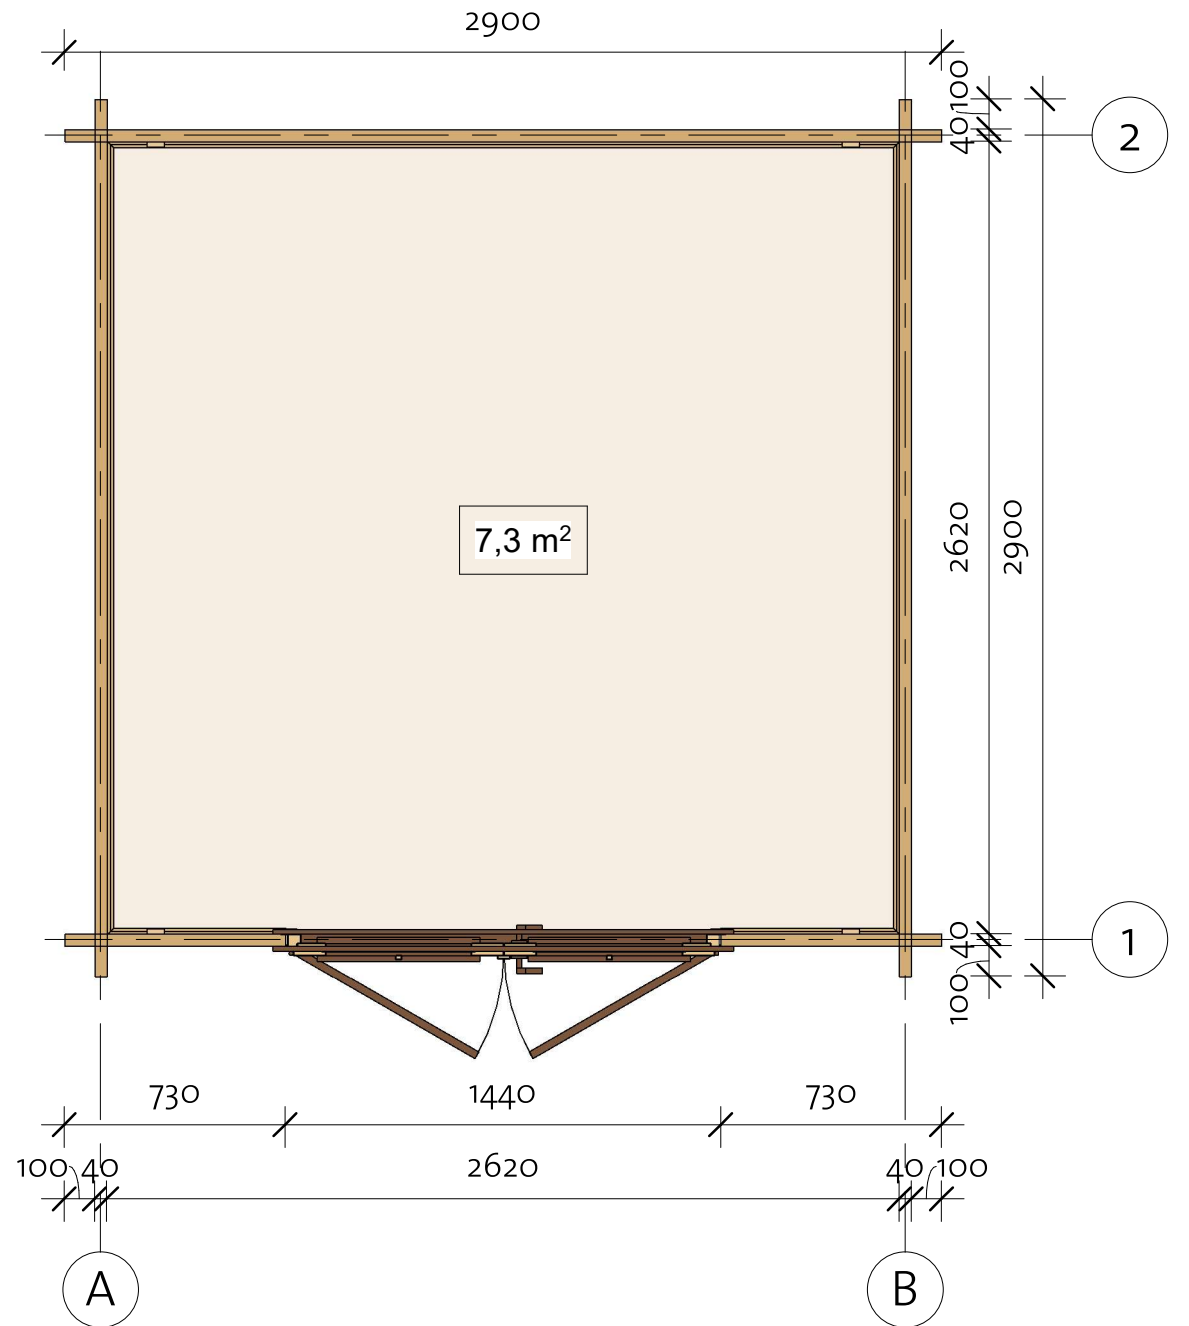


Gloria D 40 (270x270)

Wall 1

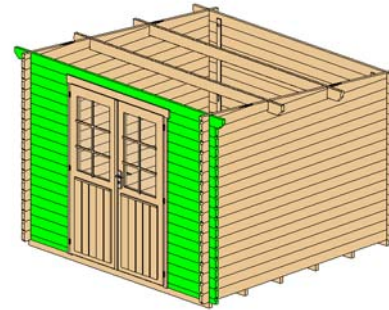

Wall 1			
Mark	Profile	Count	Cut Length
1BL-1	40X57	2	730
1LG-1	40X114	34	730
1TL 1	40X114	1	3100

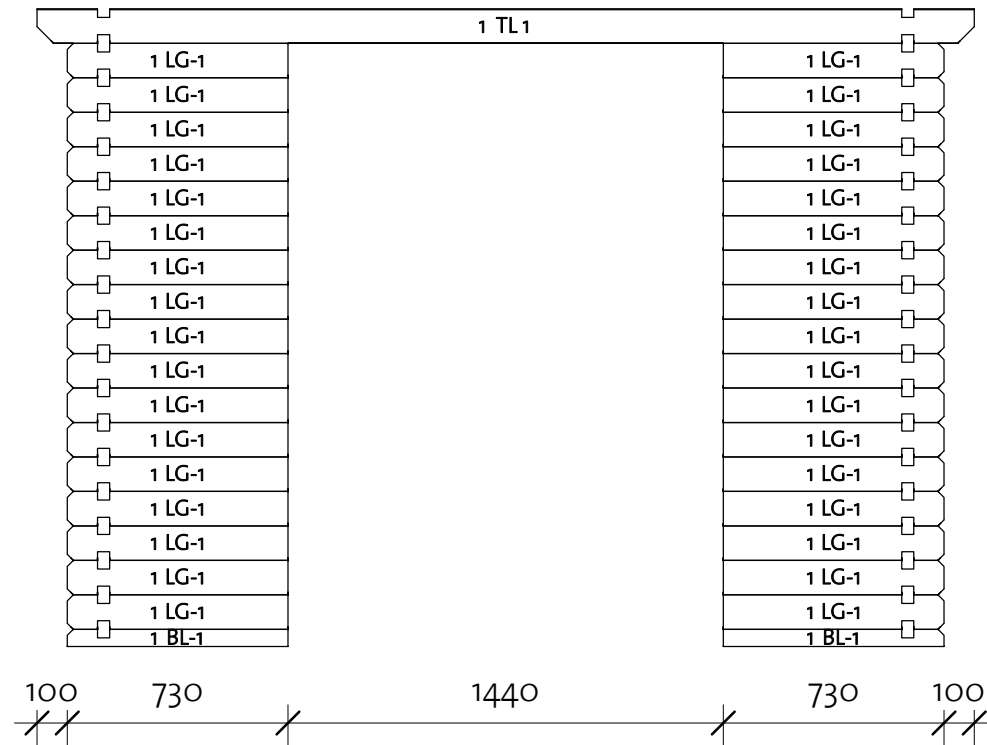


Log Profile Wall 1	
Profile	Profile

40X57	
40X114	
40X114	


Gloria D 40 (270x270)

Wall 2

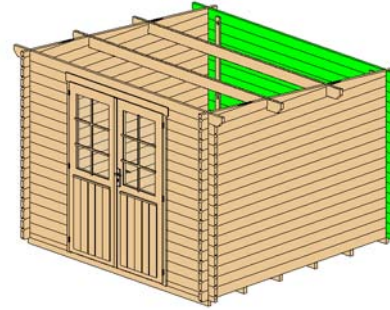

Wall 2			
Mark	Profile	Count	Cut Length

2BL-1	40x57	1	2900
2LG-1	40x114	15	2900
2TL-1	40x114	1	3100

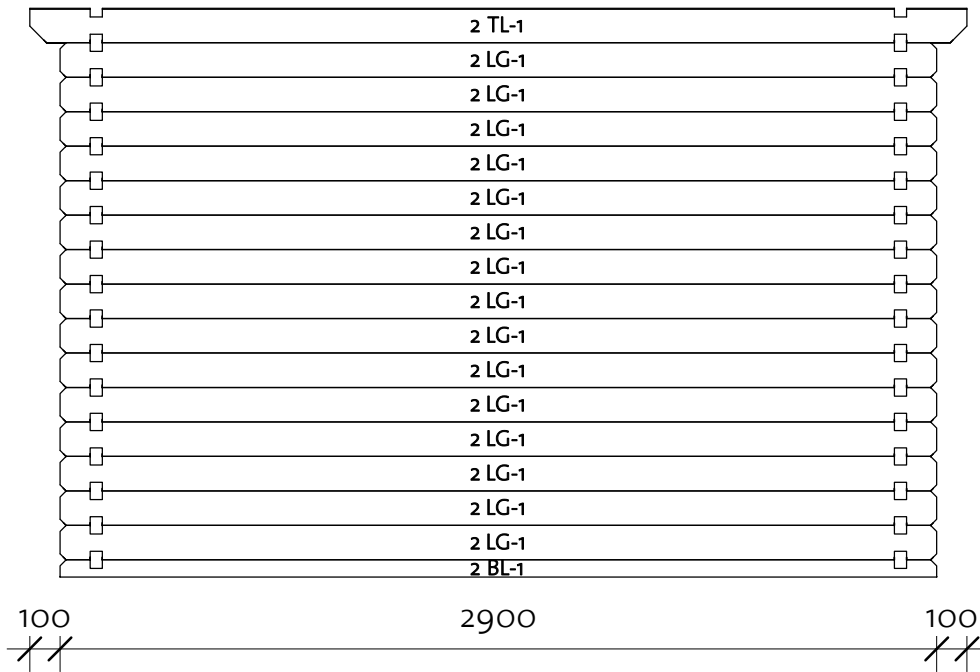


Log Profile Wall 2	
Profile	Profile

40x57	
40x114	
40x114	


Gloria D 40 (270x270)

Wall A

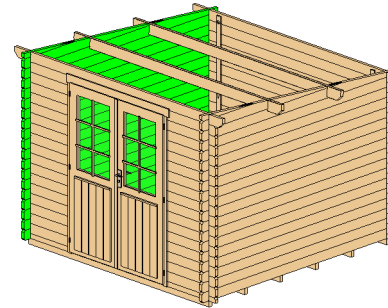


Wall A			
Mark	Profile	Count	Cut Length

ALG-1*	40x114	1	769
ALG-2*	40x114	1	2097
ALG-3*	40x114	1	2900
ALG-4	40x114	16	2900

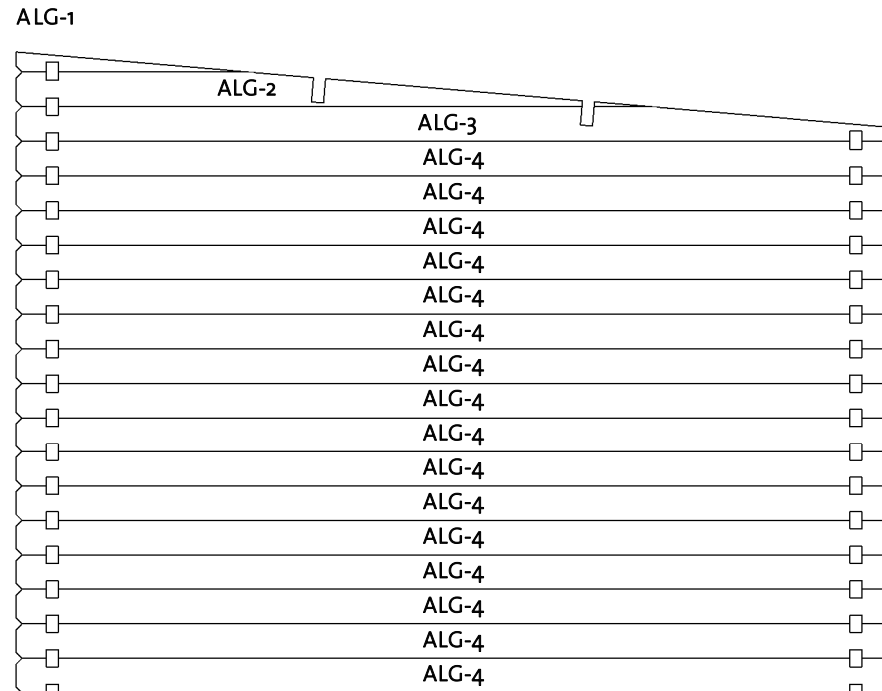


* Gable - delivered premounted

Log Profile Wall A	
Profile	Profile

40x114	
--------	---


Gloria D 40 (270x270)

Wall B

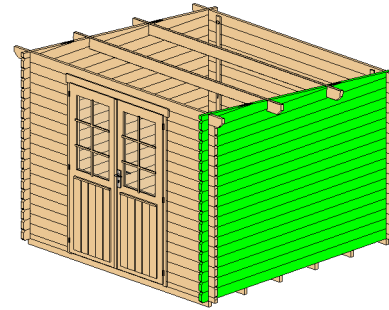


Wall B			
Mark	Profile	Count	Cut Length

BLG-1*	40x114	1	769
BLG-2*	40x114	1	2097
BLG-3*	40x114	1	2900
BLG-4	40x114	16	2900

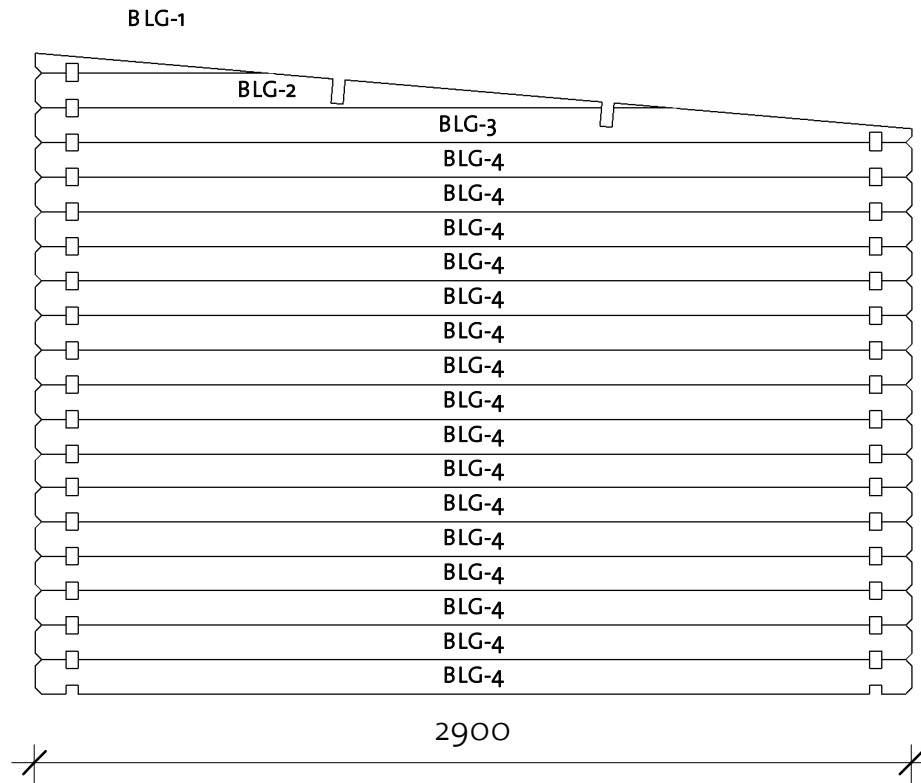


* Gable - delivered premounted



Log Profile Wall B	
Profile	Profile

40x114	
--------	---

Gloria D 40 (270x270)




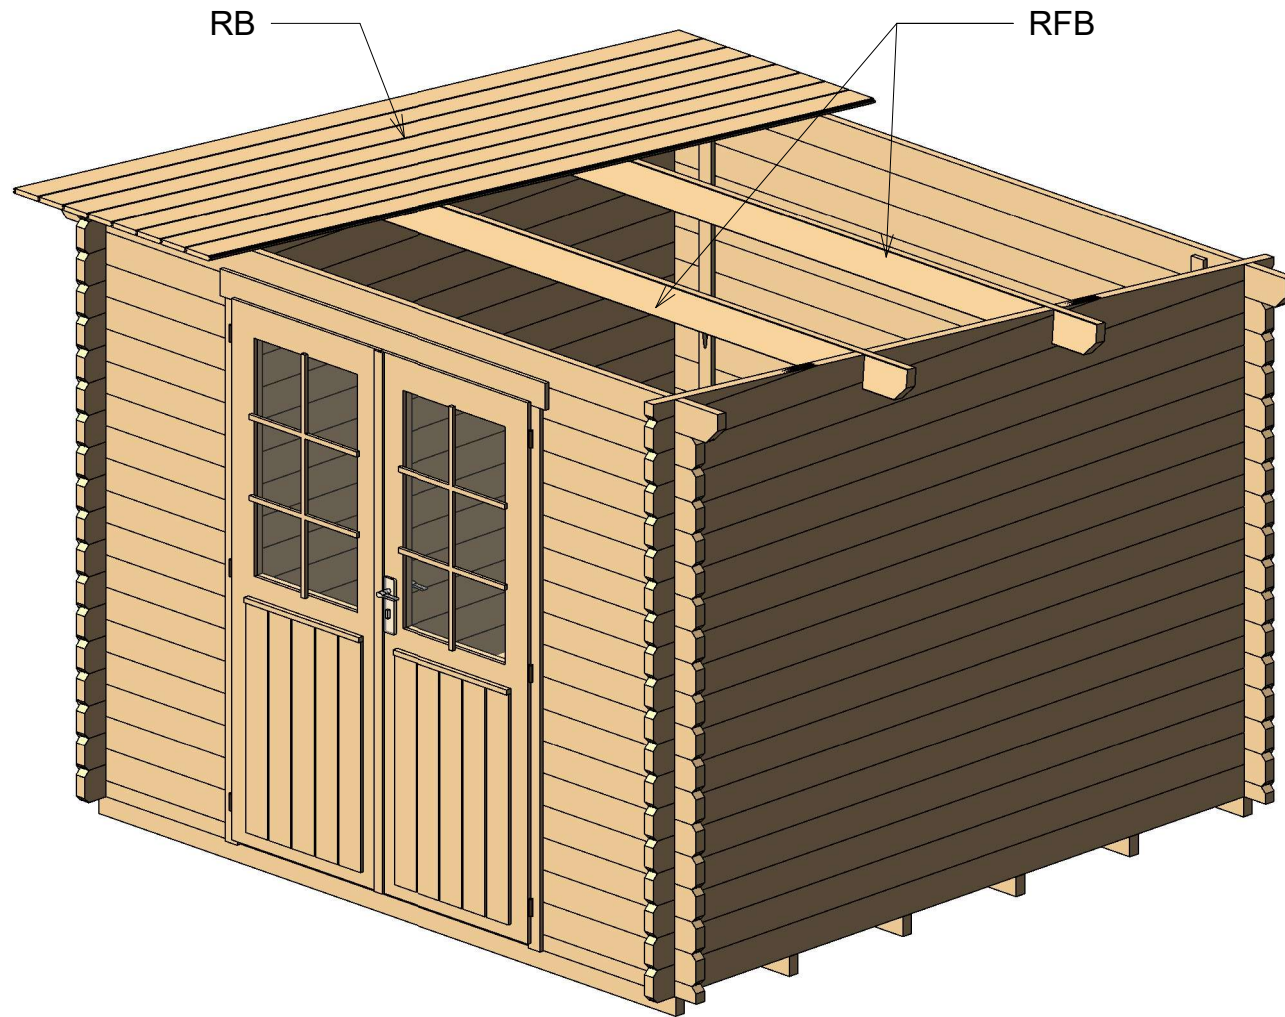
Roof 1



Roof				
Mark	Type	Profile	Count	Length
RFB	Beam 40x120		2	3100
RB	17x114		28	3122

Gloria D 40 (270x270)

Roof 2

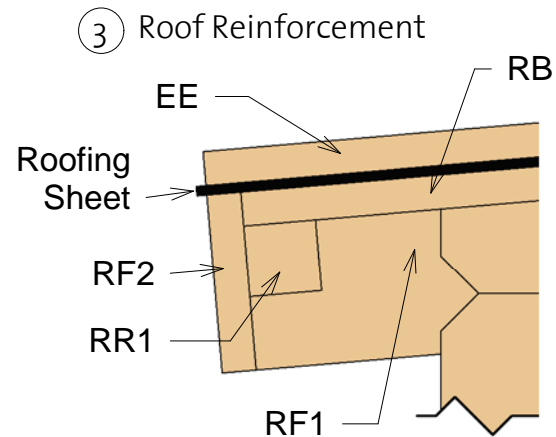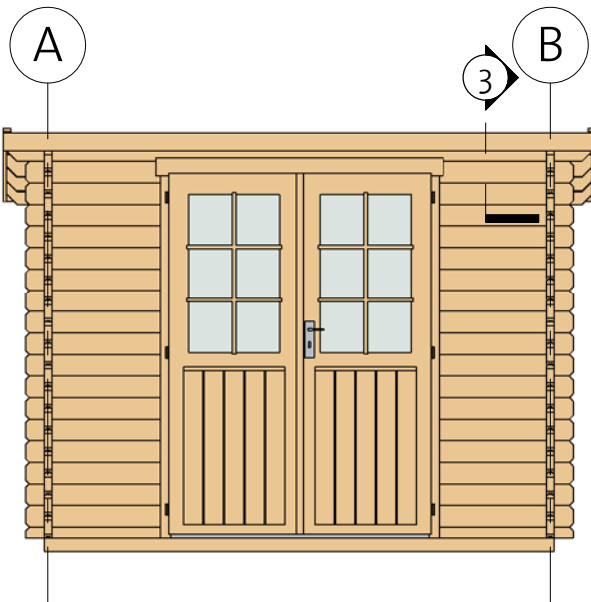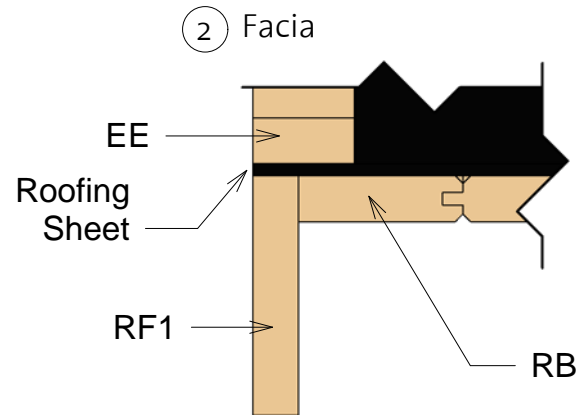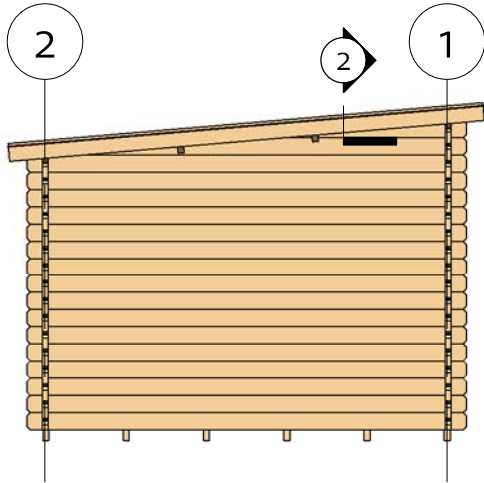


Fascia Schedule

Mark	Type	Profile	Count	Length
EE	Eave Edging 18x40		2	3156
RF1	Roof Fascia 18x95		2	3120
RF2	Roof Fascia 18x95		2	3100
RR1	Roof reinforcement 38x38		2	3100

Gloria D 40 (270x270)

Extras

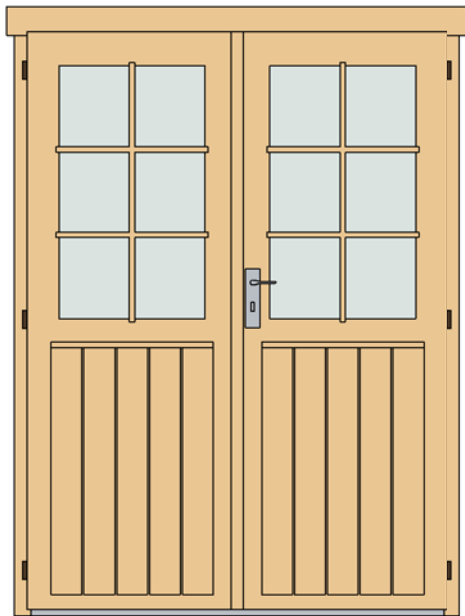

Door Schedule				
Model	Type	Width	Height	Count
CDD1R	Classic double door 1 right	1425	1955	1
DCB6	Door crossbar 6	--	--	2

Fasteners & Extras		
Name	Comments	Count

Hitblock	300-400 mm	
Bolts	M8 x 70	12
Screws	5,0 x 70	20
Screws	6,0 x 140	25
Nails	1,4 x 40	30
Screws	4,0 x 40	60
Screws	4,0 x 50	300

Windboard		
Family	Count	Length


Windboard 18x40	4	2200
-----------------	---	------




Gloria D 40 (270x270)


List of all items 1

Impregnated foundation beams				
Mark	Type	Profile	Count	Length


IFB	IFB 40x70		6	2700
-----	--------------	---	---	------

Floor Schedule				
Mark	Type	Profile	Count	Length





FB	FB 17x114		24	2617
----	-----------	---	----	------

BB	BB 20x40		4	2700
----	-------------	---	---	------

Roof				
Mark	Type	Profile	Count	Length

RFB	Beam 40x120		2	3100
-----	----------------	---	---	------

Fascia Schedule				
Mark	Type	Profile	Count	Length

EE	Eave Edging 18x40		2	3156
RF1	Roof Fascia 18x95		2	3120
RF2	Roof Fascia 18x95		2	3100
RR1	Roof reinforcement 38x38		2	3100

Gloria D 40 (270x270)

List of all items 2

Wall 1			
Mark	Profile	Count	Cut Length

1BL-1	40X57	2	730
1LG-1	40X114	34	730
1TL 1	40X114	1	3100

Wall 2			
Mark	Profile	Count	Cut Length

2BL-1	40X57	1	2900
2LG-1	40X114	15	2900
2TL-1	40X114	1	3100




Wall A			
Mark	Profile	Count	Cut Length

ALG-1*	40X114	1	769
ALG-2*	40X114	1	2097
ALG-3*	40X114	1	2900
ALG-4	40X114	16	2900

Wall B			
Mark	Profile	Count	Cut Length

BLG-1*	40X114	1	769
BLG-2*	40X114	1	2097
BLG-3*	40X114	1	2900
BLG-4	40X114	16	2900

Log Profiles	
Profile	Profile

40X57	
40X114	
40X114	

* Gable - delivered premounted
